

# Project Planning Phase

## Project Planning Template (Product Backlog, Sprint Planning, Stories, Story Points)

|               |                                                                                    |
|---------------|------------------------------------------------------------------------------------|
| Date          | 10 September 2026                                                                  |
| Team ID       | Individual Project                                                                 |
| Student Name  | Morla Jahnavi                                                                      |
| Project Name  | An Employee Requests Installation of Licensed Software through the Service Catalog |
| Maximum Marks | 5 Marks                                                                            |

### 1. Planning Logic

- The project follows Agile planning by dividing the ServiceNow solution into small functional epics and user stories that can be completed within fixed sprints.
- Story points represent relative effort and complexity using Fibonacci-style values of 1, 2, 3 and 5.
- Two sprints are planned for the individual project, with a target capacity of approximately 16 story points per sprint.

### 2. Product Backlog and Sprint Schedule

| Sprint   | Functional Requirement (Epic) | User Story No. | User Story / Task                                                                                               | Story Points | Priority | Team Member |
|----------|-------------------------------|----------------|-----------------------------------------------------------------------------------------------------------------|--------------|----------|-------------|
| Sprint-1 | Service Catalog Setup         | USN-1          | As an employee, I can find and open the licensed software request from the Service Catalog.                     | 3            | High     | Jahnavi     |
| Sprint-1 | Service Catalog Setup         | USN-2          | As an employee, I can enter the software name, version, business justification and urgency in the request form. | 3            | High     | Jahnavi     |
| Sprint-1 | Request Submission            | USN-3          | As an employee, I can submit the completed software request and receive a submission confirmation.              | 2            | High     | Jahnavi     |
| Sprint-1 | Workflow Automation           | USN-4          | As the system, I can start the configured workflow and route the request to the required approver.              | 5            | High     | Jahnavi     |
| Sprint-1 | Request Tracking              | USN-5          | As an employee, I can view the generated Request and Requested Item records for my submission.                  | 3            | High     | Jahnavi     |
| Sprint-2 | Fulfillment Automation        | USN-6          | As the system, I can create a Catalog Task for Software Support after the request is approved.                  | 5            | High     | Jahnavi     |
| Sprint-2 | Notifications                 | USN-7          | As an employee, I can receive a notification when my software request is submitted and when its status changes. | 2            | Medium   | Jahnavi     |
| Sprint-2 | Task Management               | USN-8          | As IT Support, I can update the Catalog Task through Open, Work in Progress and Completed states.               | 3            | High     | Jahnavi     |
| Sprint-2 | Testing & Validation          | USN-9          | As the project owner, I can verify the complete request, approval, fulfillment and notification workflow.       | 3            | High     | Jahnavi     |
| Sprint-2 | Documentation & Demo          | USN-10         | As the project owner, I can document the configured process and demonstrate request status tracking.            | 3            | Medium   | Jahnavi     |

3. Project Tracker and Sprint Plan

| Sprint   | Total Story Points | Duration | Sprint Start Date | Sprint End Date (Planned) | Story Points Completed | Release / Review Date |
|----------|--------------------|----------|-------------------|---------------------------|------------------------|-----------------------|
| Sprint-1 | 16                 | 5 Days   | 22 Sep 2026       | 26 Sep 2026               | 16                     | 26 Sep 2026           |
| Sprint-2 | 16                 | 5 Days   | 28 Sep 2026       | 02 Oct 2026               | 16                     | 02 Oct 2026           |

4. Velocity Estimation

Velocity is calculated as the total story points completed divided by the number of completed sprints.


Total Story Points Completed = 16 + 16 = 32

Number of Sprints = 2

Velocity = 32 / 2 = 16 Story Points per Sprint

5. Burndown Chart

The burndown chart represents the work remaining during a sprint. The planned objective is to reduce the remaining story points to zero by the end of the sprint.

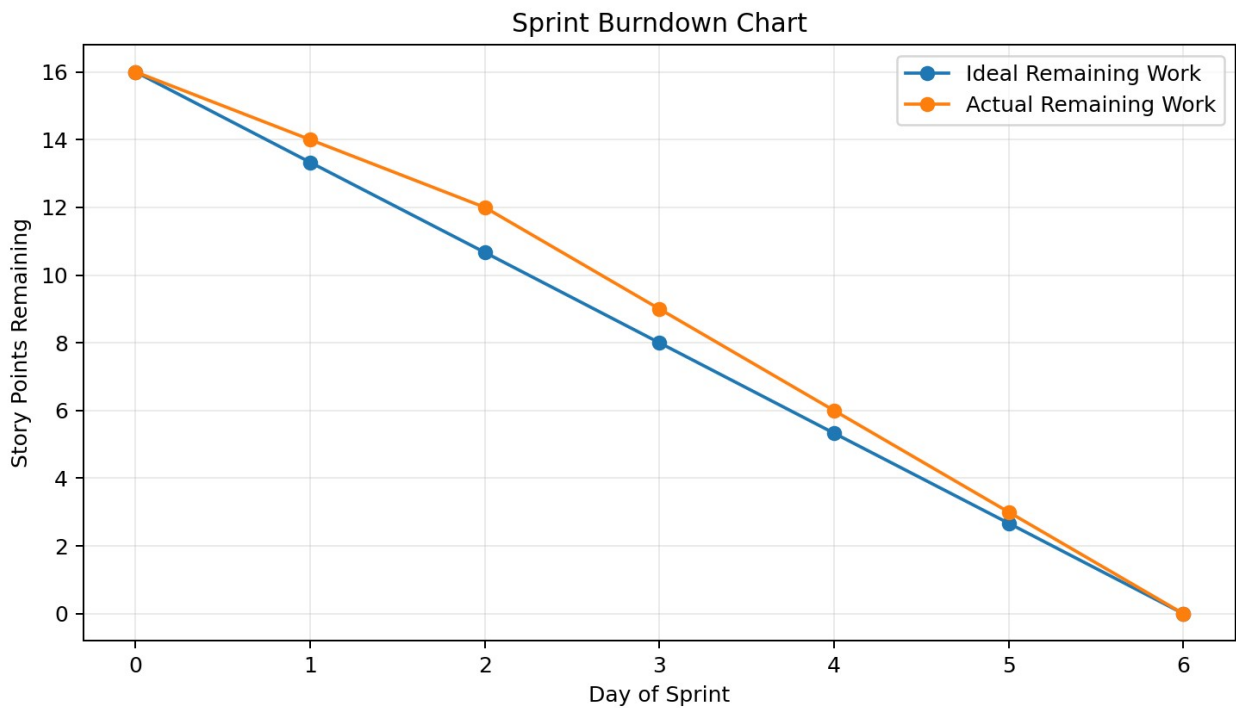

6. Planned Project Outcome

- Employees can submit licensed software installation requests through a standardized Service Catalog item.
- The ServiceNow workflow routes requests for approval and creates fulfillment tasks automatically after approval.
- Employees receive confirmation and status notifications during the request lifecycle.
- Requesters and IT Support can follow progress through Request, Requested Item (RITM) and Catalog Task records.
- The process provides clearer visibility, reduces manual coordination and supports controlled software installation.
